FORD POWERHOUSE FORD
GENERATOR WINDING DATA
#20 GAUGE MAGNET WIRE
103 TURNS
4.2 OHMS (ASSEMBLY)
CW=SOUTH
CCW=NORTH
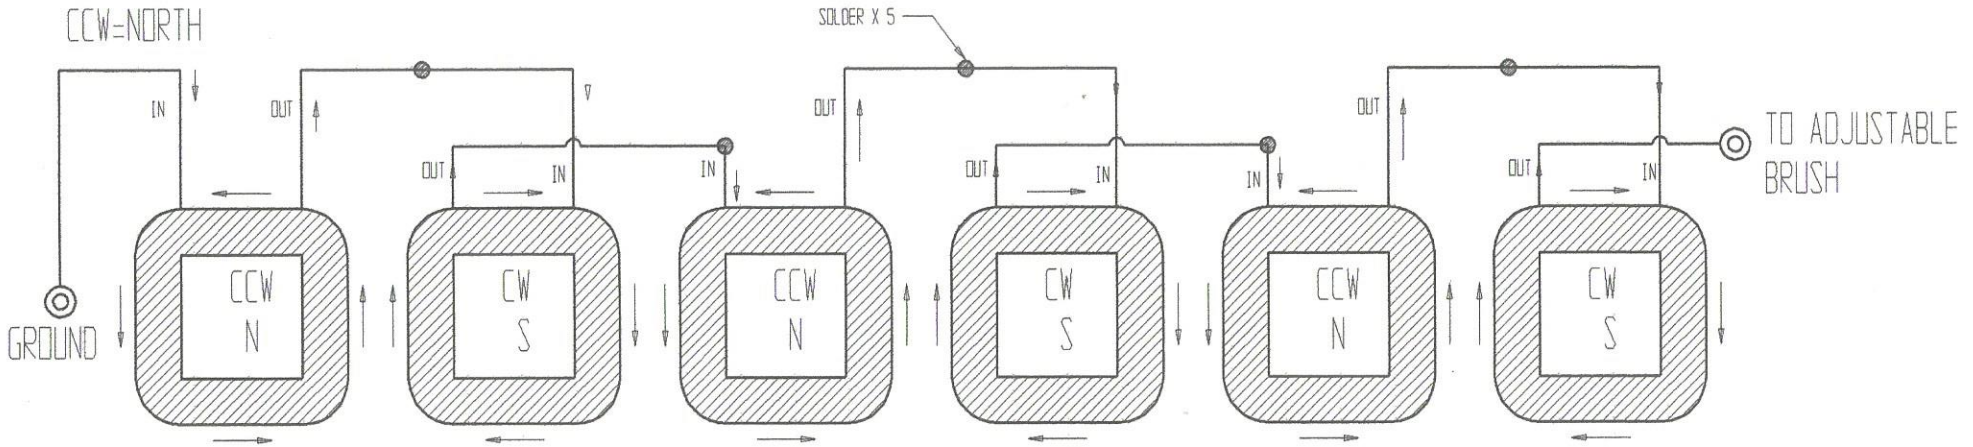
WHEN I FIRST INSTALLED THE FIELD WINDING'S
THE MOTOR MOTORED IN THE WRONG DIRECTION.
ALL I NEEDED TO DO WAS REVERSE THE FIELD
LEADS AND THAT WORKED.
